


NAME- PRADYUMNA P


SRN- PES2UG24CS359

Agile Backlog Creation & Sprint Simulation in Jira

1-LIST OF EPICS CREATED

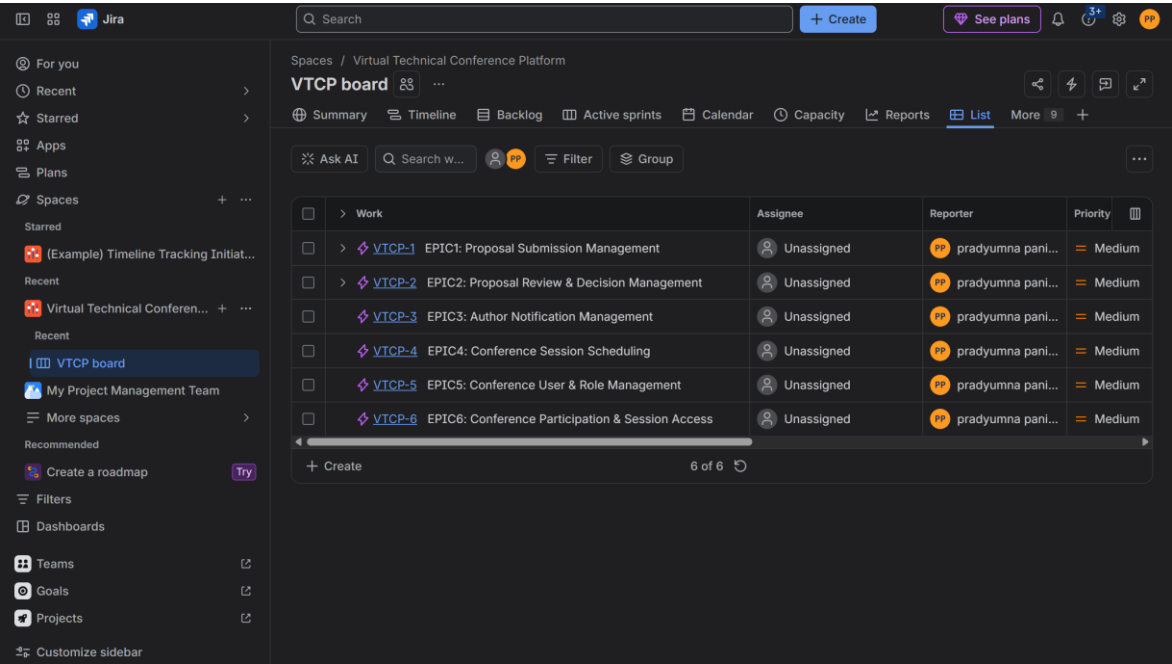

2- LIST OF USER STORIES UNDER EPIC

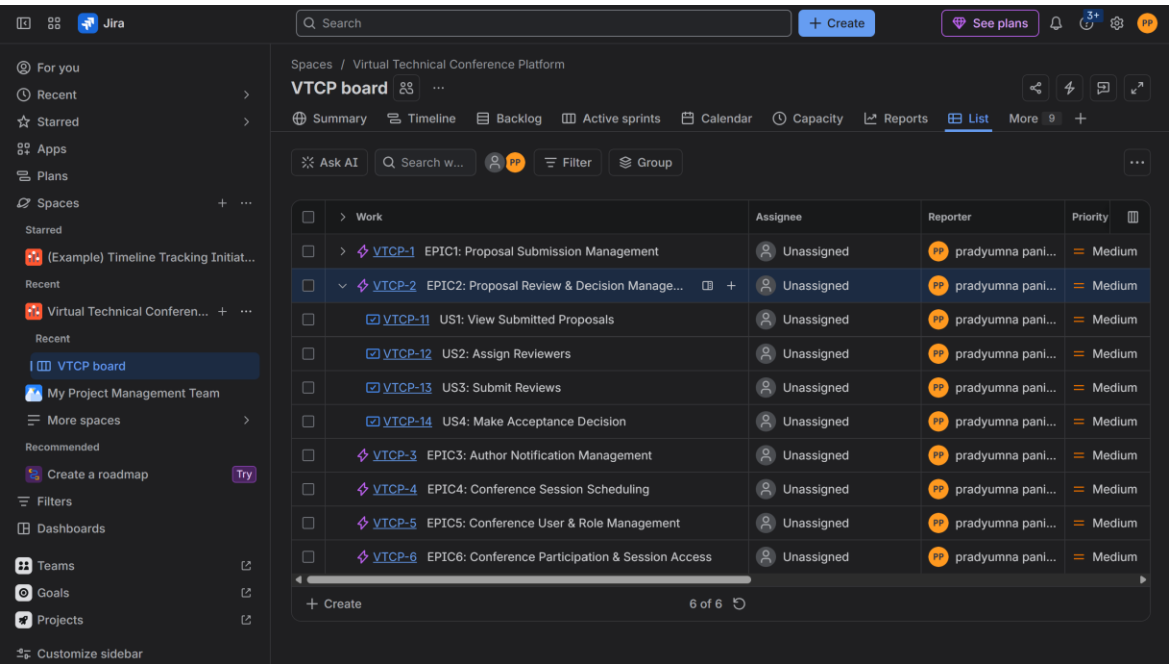

3- BACKLOG DASHBOARD (CREATING SPRINTS)

The screenshot displays the Jira Backlog dashboard for the 'Virtual Technical Conference Platform' space. The dashboard is titled 'VTCP board' and shows a list of work items under 'VTCP Sprint 3' and a 'Backlog' section. The left sidebar contains navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Filters', 'Dashboards', 'Teams', 'Goals', and 'Projects'.

VTCP Sprint 3 (2 work items)

Item	Summary	EPIC	Status	Estimate
VTCP-12	US2: Assign Reviewers	EPIC2: Proposal R...	To Do	3
VTCP-13	US3: Submit Reviews	EPIC2: Proposal R...	In Progress	5

Backlog (4 work items)

Item	Summary	EPIC	Status	Estimate
VTCP-7	US1: Enter Proposal Details	EPIC1: Pr...	To Do	3
VTCP-8	US2: Upload Proposal File	EPIC1: Pr...	To Do	3
VTCP-11	US1: View Submitted Proposals	EPIC2: Pr...	To Do	3
VTCP-14	US4: Make Acceptance Decision	EPIC2: Pr...	To Do	5

4- ACTIVE SPRINTS

The screenshot displays the Jira Active Sprints dashboard for the 'Virtual Technical Conference Platform' space. The dashboard is titled 'VTCP board' and shows a Kanban board with columns for 'TO DO', 'IN PROGRESS', and 'DONE'. The left sidebar contains navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Filters', 'Dashboards', 'Teams', 'Goals', and 'Projects'.

TO DO


IN PROGRESS (2)

Item	Summary	EPIC	Status	Estimate
VTCP-12	US2: Assign Reviewers	EPIC2: Proposal Review & Decision Manag...	In Progress	3
VTCP-14	US4: Make Acceptance Decision	EPIC2: Proposal Review & Decision Manag...	In Progress	5

DONE (1)

Item	Summary	EPIC	Status	Estimate
VTCP-13	US3: Submit Reviews	EPIC2: Proposal Review & Decision Manag...	Done	5

5- BURNDOWN CHART

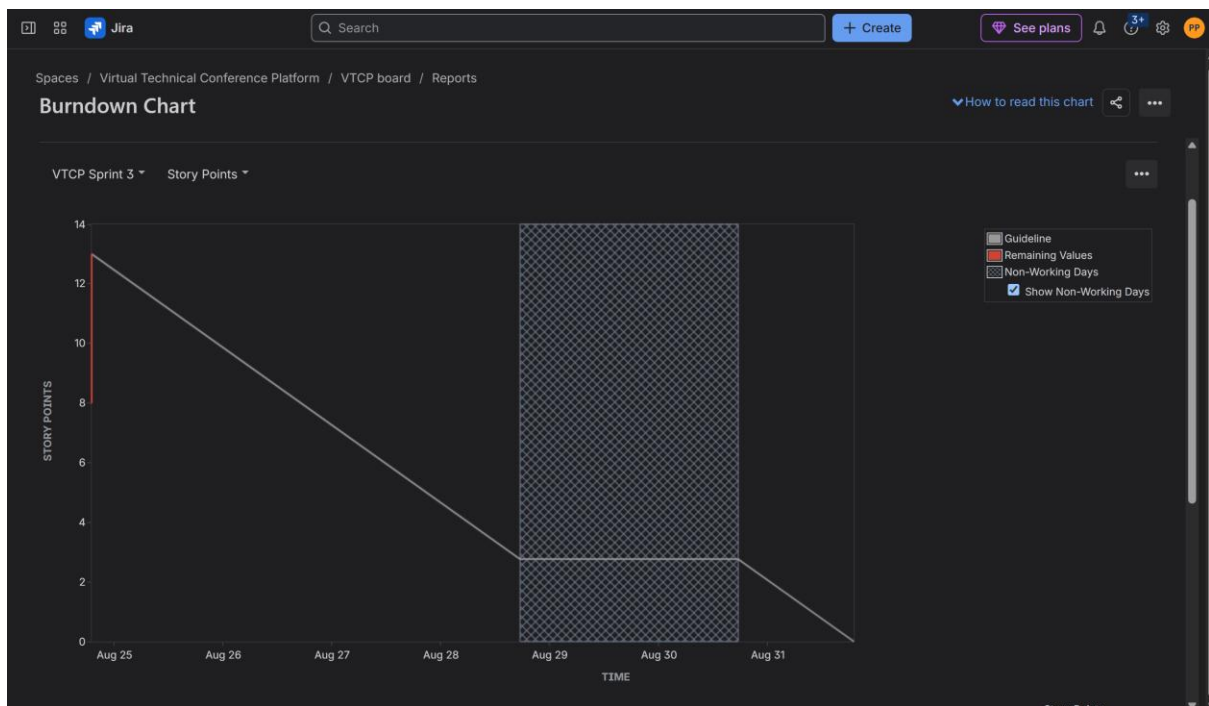

REFLECTION QUESTIONS

Q1) Did your estimations reflect the actual effort?

ANS-The initial estimations did not accurately reflect the actual effort due to underestimation and mid-sprint scope changes. Although the sprint was initially planned for 8 story points (VTCP-12 and VTCP-13), VTCP-14 was pulled in from the backlog to bring the total commitment to 13 points. The team only completed 5 story points (VTCP-13), leaving 8 story points trapped in "In Progress," which demonstrates that the real complexity and workload needed to finish multiple stories were underestimated relative to the team's actual capacity.

Q2) Was your backlog well-prioritized?

ANS-The backlog lacked proper prioritization and violated core functional dependencies. Essential foundational tasks—such as all of Epic 1 (Proposal Submission) and US1 of Epic 2 (*View Submitted Proposals*)—were left in the product backlog while downstream actions like assigning reviewers and making acceptance decisions were pulled into the sprint. Furthermore, highest-priority items were initially bypassed, resulting in mid-sprint backlog leakage where downstream tasks were attempted before their prerequisites were implemented.

Q3) How did your simulated sprint align with your plan?

ANS-The simulated sprint deviated significantly from the initial plan due to unplanned scope expansion and execution bottlenecks. The scope surged mid-sprint from 2 items (8 story points) to 3 items (13 story points), marking a substantial increase over the original commitment. Execution fell short as only 1 out of the 3 active user stories was delivered to "Done," leaving 61.5% of the total sprint points incomplete and stalled in "In Progress" at the end of the sprint cycle.

Q4) What insights did the burndown chart give about your team's capacity?

ANS-The burndown chart indicates that the team overcommitted beyond its true delivery capacity, with an actual velocity closer to 5 story points per sprint rather than the attempted 13 points. After an initial drop from 13 down to 8 points on day one, the burndown line flatlined across the remaining sprint duration (Aug 26–Aug 31) with zero further progress toward zero. This stagnation highlights that the team's capacity was diluted across multiple parallel in-progress tasks instead of focusing on finishing tasks sequentially.
